


# REBUILDING I-93 SALEM TO MANCHESTER



## 14633B: NB & SB MAINLINE WIDENING WEIGH STATION TO KENDALL POND ROAD

PROJECT FACT SHEET

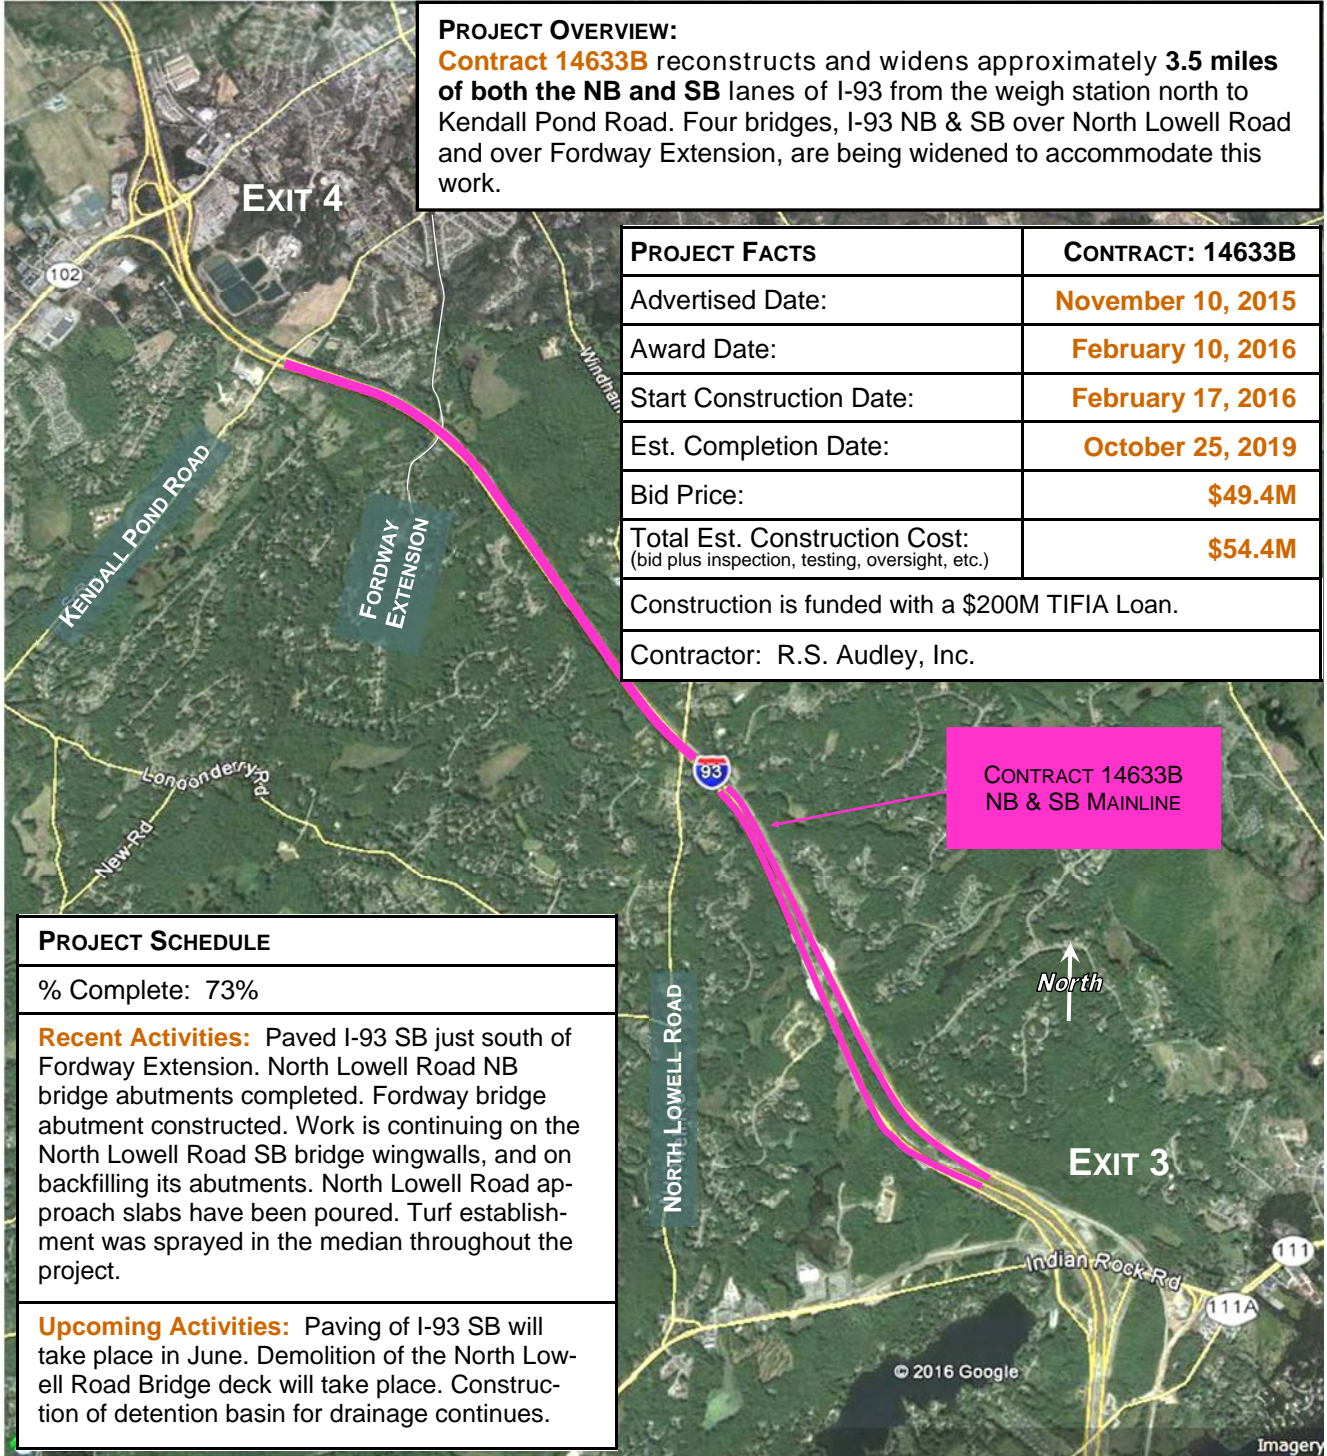

**PROJECT OVERVIEW:**

**Contract 14633B** reconstructs and widens approximately **3.5 miles of both the NB and SB** lanes of I-93 from the weigh station north to Kendall Pond Road. Four bridges, I-93 NB & SB over North Lowell Road and over Fordway Extension, are being widened to accommodate this work.

PROJECT FACTS	CONTRACT: 14633B
Advertised Date:	<b>November 10, 2015</b>
Award Date:	<b>February 10, 2016</b>
Start Construction Date:	<b>February 17, 2016</b>
Est. Completion Date:	<b>October 25, 2019</b>
Bid Price:	<b>\$49.4M</b>
Total Est. Construction Cost: (bid plus inspection, testing, oversight, etc.)	<b>\$54.4M</b>
Construction is funded with a \$200M TIFIA Loan.	
Contractor: R.S. Audley, Inc.	

PROJECT SCHEDULE
% Complete: 73%
<b>Recent Activities:</b> Paved I-93 SB just south of Fordway Extension. North Lowell Road NB bridge abutments completed. Fordway bridge abutment constructed. Work is continuing on the North Lowell Road SB bridge wingwalls, and on backfilling its abutments. North Lowell Road approach slabs have been poured. Turf establishment was sprayed in the median throughout the project.
<b>Upcoming Activities:</b> Paving of I-93 SB will take place in June. Demolition of the North Lowell Road Bridge deck will take place. Construction of detention basin for drainage continues.

Updated: 6-27-18



[RebuildingI93.com](http://RebuildingI93.com)







**ABOVE: SB NORTH LOWELL ROAD BRIDGE BACK-FILLING**

**UPPER RIGHT: DRAINAGE DETENTION BASIN**

**MIDDLE RIGHT: INSTALLATION OF ROCK BOLTS AND DOWELS IN SOUTHERN LEDGE CUT**

**LOWER RIGHT: HAND SCALING**



14633B



[RebuildingI93.com](http://RebuildingI93.com)

MOVING  
AHEAD
